



OFFICE OF THE CITY MANAGER

TO: Honorable Mayor and Members of the City Council

FROM: Patrick Urich, City Manager *Patrick Urich*

DATE: April 19, 2013

SUBJECT: Issues Update

The following is a report related to the City for the weekly Issues Update. If there are additional items you believe should be included, please let me know.

March 2013 Marriott Pere Marquette Report

Attached, please find the observation and progress report for the Marriott Pere Marquette project.

Marriott Hotel Projects

March 2013 Progress Report



Report Dated: April 12, 2013



Marriott Hotel Projects Progress Report


This is the monthly report prepared by Dewberry Architects Inc. for the month of March 2013. It covers construction activities for the four components of the project; parking deck, pedestrian bridge, Pere Marquette Hotel, and the Marriott Courtyard Hotel. The ePrismSoft Compliance System Executive Summary Report, dated April 10, 2013, for EEO monitoring is attached.

Parking Deck

Progress Summary:

The parking deck is substantially complete and has been opened for business.

Photos:

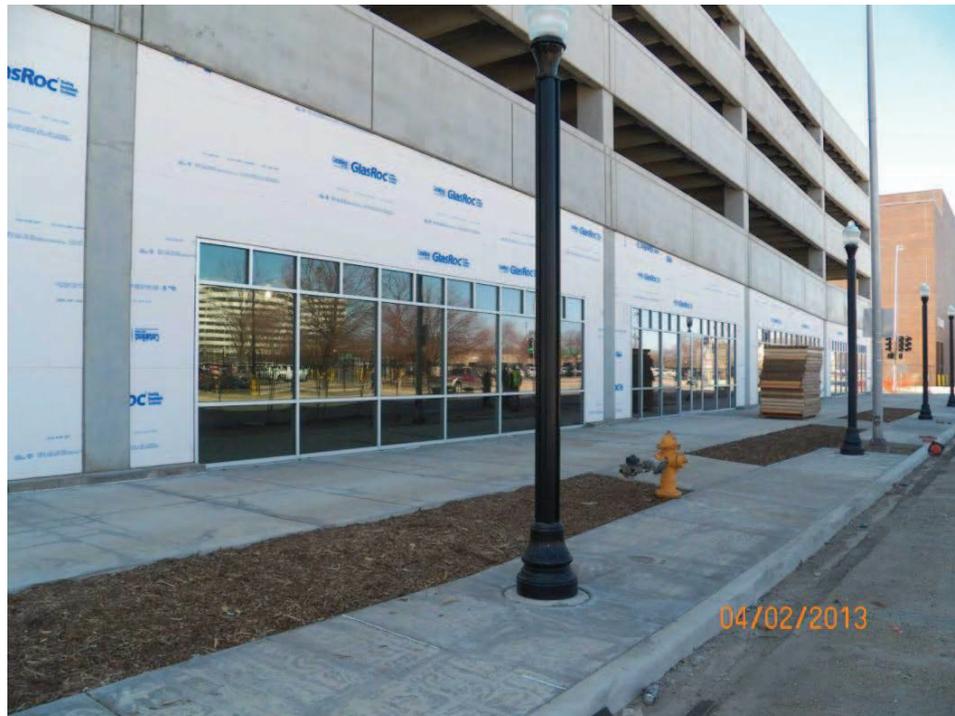

Retail spaces and new street lights along Monroe Street

Pedestrian Bridge


Progress Summary:

The concrete foundation and support wall have been installed. Existing sewer lines discovered during the excavation were relocated. The steel framing at the parking deck is installed. A temporary walkway was installed on the Civic Center side for pedestrian access around the construction area.

Forthcoming Items:

Progress has stopped awaiting the approval of the air easement. This is to be on the City Council agenda for April 23rd.

Photos:

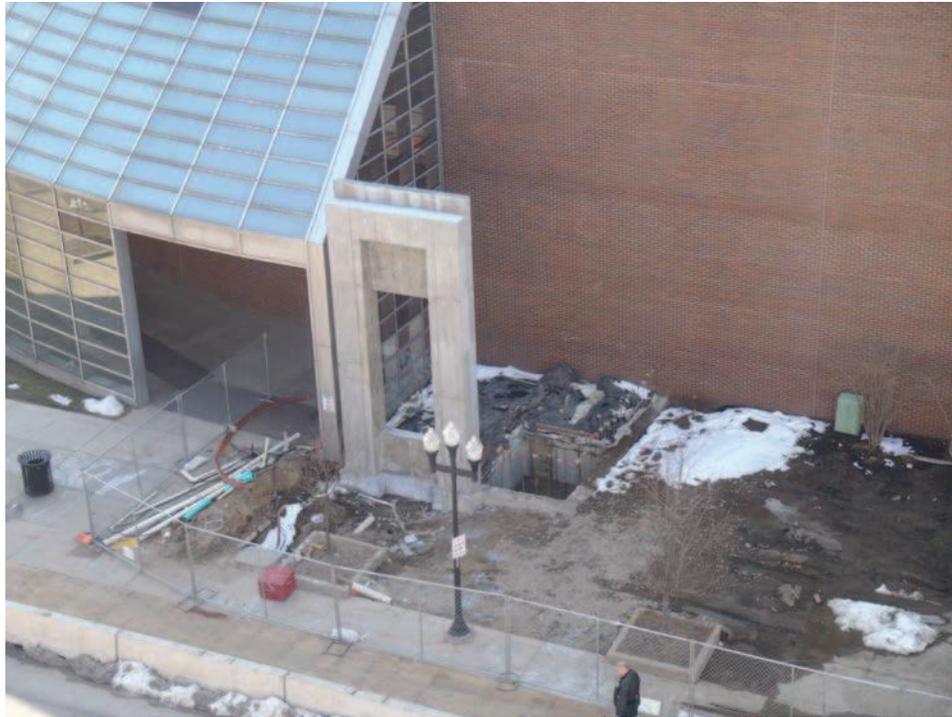

Foundation and supporting wall

Pere Marquette Hotel

Progress Summary:

The renovation work on the passenger elevators is nearly complete. Certification of the passenger elevators is anticipated in mid-April. Finish work in the basement, first floor and second floor continue, along with MEP trim out. Some of the ballrooms are nearing completion. Laundry and Kitchen equipment has been delivered to the site and is in the process of being connected. Cleaning is ongoing throughout the building. FFE installation continues. The 7th through 10th floors are ready for punchlist. Guest room carpet and door frames are being installed on the 11th floor. Drywall installation is underway on the 12th floor, as well as, patching of the exterior walls. Painting on the 12th floor should start in early April.

Individual guest room heat pumps have been commissioned and are operational on the 3rd through 10th floors. Life safety, including smoke evacuation systems are being installed and are anticipated to be started up in early April. New hot water heaters are being installed in the basement. The water softeners are installed. All mechanical equipment on the 13th floor and tower roof has been commissioned and started. MEP rough-ins are complete. The last of the mechanical equipment for the ballrooms has been installed and final connections are being made. The cooling tower for this portion of the building should be commissioned mid to late April.

Roofing work has on the low is complete. The coating called for on the existing roofing to remain is being reviewed due to the condition of some parts of the existing roof.

Forthcoming Items:

Hotel employees are anticipated to be on site starting in mid-April to get guestroom and other areas ready for use. FF&E items will continue to be shipped including some of the specialty vanities and light fixtures.

The engineers are working with the City on the sidewalk slope issue.

Photos:



Finishes in Chiminee Ballroom



Front desk at 1st floor



Tile installation at bar on 1st floor



Railing installation at Grand Stair



FFE installation on the 3rd floor



Door installation on 11th floor



Hot water tank installation in basement



Walk-in freezer/cooler in 1st kitchen



Tile installation at 1st floor



Wood flooring installation at 1st floor



Ceiling at 1st floor



Plumbing fixture installation at 1st floor restrooms

Courtyard

Progress Summary:

Demolition of the buildings is complete. Storm sewer piping has been installed, inspected, and backfilled. Site being filled and tested to bring for preparation of foundations.

Forthcoming Items:

Work is being value engineered in hopes of reducing construction cost due to current favorable bidding climate. Work is planned to resume once pricing is finalized.

Photos:



Storm sewer installed and backfilled



Site preparation for foundation work

Schedule

The construction schedule for the Pere Marquette was adjusted to June 2013. Current targeted milestones are listed below.

Milestones:

Parking Deck	Open
Pere Marquette Substantial Completion	June 2013
Pere Marquette Opening	End of June 2013 (Contingent on Marriott)

Financial

The project construction costs remain within budget. There were no new change orders this month. The construction contract with Core Construction Services, Inc. covers the construction of the parking deck, pedestrian bridge, the Pere Marquette, and the Courtyard by Marriott. Change orders adding food service equipment (\$600,000) and new water heaters, tanks, and AHUs (\$500,000) were approved and added to the contract.

Construction Cost Status

(Includes pay application No. 13 for the month of March 2013)

Original Contract Sum	\$44,000,000.00
Net Change Orders	\$2,314,148.00
Contract Sum to Date	\$46,314,148.00
Total Complete to Date	\$30,818,651.57
Percent Complete	66.5%
Retainage	\$2,839,527.08
Total Paid to Date	\$27,979,124.49
Balance to Finish	\$18,335,023.51

EEO

Project Goals:

Enterprise Level:	10% MBE and 5% WBE
Labor Utilization:	18% Minority and 3% Female

Progress Summary:

Verified MBE firms under contract have increased slightly to 9.83% of the total construction cost. Due to the multiple phase nature of the project, only approximately \$38.5 million of the \$45 million value has been committed (contracted). Comparing the current MBE contracts to the total committed, the MBE portion still represents 11.51%. In addition there are currently 4 non-verified MBE firms. These are firms that are under contract and are having their status confirmed. Efforts are continuing to contract additional MBE firms for portions of the uncommitted (non-contracted) work.

For the WBE portion; J. Hulick Electric, Inc. and Connies Commercial Cleaning are identified. The WBE contracted value is at 7.14%. Connie's Commercial Cleaning is both a MBE and WBE and is reflected in both Contracted Values. Since the value cannot be counted twice in the subtotal, \$60,000 has been subtracted to arrive at the \$38,530,554.80 subtotal.

The Human Capital Development report now also includes confirmed payments to MBE and WBE firms, as well as, a breakdown of payments by demographic group. For the MBE and WBE firms, this is indicated as the “Actual Value” and is reflected in the chart below. As anticipated, these figures continue to increase as contractors are paid.

Enterprise Level Summary (Project Goals: 10% MBE and 5% WBE)

Current results based on Human Capital Development, LLC Executive Contract Summary Report dated 4/10/ 2013.

	Contracted Values	Percentage of Total Contract	Percentage of Committed Work	Actual Value (Confirmed Payments)
MBE	\$4,446,398.00	9.83%	11.54%	\$3,398,221.09
WBE*	\$3,226,233.00	7.14%	8.37%	\$1,330,498.33
NON-VERIFIED Minority	\$17,946.25	0.04%	0.05%	\$14,562.25
NON-MINORITY	\$30,899,977.55	68.34%	80.20%	\$20,976,138.75
COMMITTED WORK (Subtotal)	\$38,530,554.80	85.22%	100.16%	\$25,663,474.00
UNCOMMITTED WORK**	\$6,683,593.20	14.78%		
TOTALS	\$45,214,148.00	100.00%		

* See discussion above concerning WBE.

**The Uncommitted Work is work for which there are no contracts yet.

Minority labor utilization is near goal at 17.57% and the Female utilization is at 3.73%. The minority labor utilization had been falling slightly for several months, but has shown a slight increase this month. The contractor is aware of this and is continuing to make efforts to increase the utilization.

Labor Utilization Summary (Project Goals: 18% Minority and 3% Female)

Current results based on Human Capital Development, LLC Executive Contract Summary Report dated 4/10/ 2013.

	Current Labor Hours	Percentage of Total
Minority	35,836.55	17.57%
Female	7,607.00	3.73%
Non-Minority/Female	162,243.30	79.53%
Total	204,003.35	

Please note when reviewing the Human Capital Development report in the Labor Utilization chart that the total for line items Minority, Female, and Non-Minority/Female shows as 204,003.35 hours, however, the hours listed for these lines adds up to 205,686.85 hours. There are 1,683.5 female minority hours that are reported under both the Female and Minority items. Since these hours cannot be counted twice for the total, 1,683.5 hours has been subtracted out to arrive at the 204,003.35 hour total. Adding the 1,683.5 hours to the 204,003.35 equals 205,686.85 hours which is the same total arrived at by adding the hours reported for each line item.

Also, when reviewing the Human Capital Development report you will note a difference between the total number of employees of each Demographic Employment Breakdown and the employee count shown in the Demographic Summary Chart. This difference is due the fact that some employees perform more than one trade tasks listed in the Demographic Employment Breakdown. As an example, the Black Demographic Employment Breakdown shows 64 males for a total of 16,287.55 hours. When you look at

the Demographic Summary chart under Black Male, you see a count of 56 for 16,287.55 hours. Each Demographic Employment Breakdown Chart shows how many employees perform which tasks while the Demographic Summary chart shows the total number of employees within a specific demographic.

In the Human Capital Development report you will find the current List of Subcontractors that list all those subcontractors under contract. Please note that this list indicates each contractor's gross contract amount. Some of the contractors are subcontractors to other contractors on this list. The reporting software nets these values when reporting them in the Enterprise Level Summary chart.

The Human Capital Development report also includes an "Employment Breakdown: Apprenticeship Summary" chart. This chart was added in support of Illinois Project Labor Agreements Act HB 2987.

During Dewberry's periodic site visits, we have casually observed EEO participation and have found them to be consistent with the figures presented.

ePrismSoft Compliance System



Executive Contract Summary

Contract Name: Pere Marquette - Courtyard
Report Period: April 2012 to March 2013
Contractor: CORE Construction

Contract: Pere Marquette - Courtyard

Enterprise Level

Goal	Contract Planned Value	Actual Value	% of Plan	% of Actual
5.00% US - WBE or US - FBE	\$3,226,233.00	\$1,330,498.33	7.14%	2.94%
10.00% US - MBE or US - DBE	\$4,446,398.00	\$3,398,221.09	9.83%	7.52%
Total Minority Subs	\$7,612,631.00	\$4,673,046.00	16.84%	10.34%
Non- Verified Minority Subs	\$17,946.25	\$14,562.25	0.04%	0.03%
Total Non- Minority Subs	\$30,899,977.55	\$20,976,138.75	68.34%	46.39%
Amount Not Yet Allocated	\$6,683,593.20	\$0.00	14.78%	0.00%
Contract Totals	\$45,214,148.00	\$25,663,747.00	100.00%	56.76%

Non- Verified Minority Subcontractors

Contractor Name	Contract Name	Contract Amount	Contract Payments
Garcia Brothers Trucking	Garcia Brothers Trucking	\$783.75	\$783.75
CVC Trucking	CVC Trucking	\$760.00	\$760.00
Kirby Trucking	Kirby Trucking	\$1,402.50	\$1,402.50
Joseph Construction Co. of Central Illinois	Joseph Construction Co. of Central Illinois	\$15,000.00	\$11,616.00

Main Contract Change Orders

Change ID	Date	Previous Amount	Change Amount	New Amount
CO #4	12/04/2012	\$44,000,000.00	\$432,148.00	\$44,432,148.00
	01/31/2013	\$44,432,148.00	\$782,000.00	\$45,214,148.00
Total Change			\$1,214,148.00	

Labor Utilization

Goal	Labor Hours	Percent of Total
90.00% Resident Workforce in IL state	199,258.35	97.67%
18.00% Minority Workforce	35,836.55	17.57%
3.00% Female Workforce	7,607.00	3.73%
Non Minority/ Female	162,243.30	79.53%
Total Contract Hours	204,003.35	100%

Contract: Pere Marquette - Courtyard

List of Subcontractors

Contractor Name	Contract Number	Contractor Status	Contract Amount		Contract Payments	
Human Capital Development, LLC	2012	Minority	\$40,000.00	0.09%	\$15,000.00	0.03%
Scope: Consulting						
Core Construction Services of Illinois Inc.	Internal Work Order	Non-Minority	\$4,343,191.80	9.61%	\$5,899,258.78	13.05%
Scope:						
Valor Technologies, Inc.	11060-2052	Minority	\$980,000.00	2.17%	\$740,171.70	1.64%
Scope: Abatement						
Otto Baum Company, Inc.	11060-4060	Non-Minority	\$1,802,237.00	3.99%	\$1,619,410.24	3.58%
Scope: Masonry Restoration; Cast- in- Place Concrete; Paving; Excavation; Storm Sewer; Masonry						
Central Illinois Rebar Installers, Inc.	12-306-1	Minority	\$75,280.00	0.17%	\$61,502.30	0.14%
Scope:						
The PIPCO Companies, LTD.	11060-15030	Non-Minority	\$7,302,410.00	16.15%	\$5,910,104.49	13.07%
Scope: Plumbing; Fire Protection; HVAC						
Design Air Inc.	002	Minority	\$502,208.00	1.11%	\$357,068.34	0.79%
Scope: Plumbing						
VOGUE PAINTING & DECORATING	11060-9110	Non-Minority	\$1,463,105.00	3.24%	\$873,731.91	1.93%
Scope: Painting & Ceiling Patching						
Ridge Painting	13	Minority	\$500,000.00	1.11%	\$574,213.75	1.27%
Scope:						
River City Demolition	11060-2050	Non-Minority	\$358,400.00	0.79%	\$384,618.82	0.85%
Scope: Demolition						
KENNEL Trucking	KENNEL Trucking	Non-Minority	\$5,567.50	0.01%	\$5,567.50	0.01%
Scope: Trucking						
Leo Brown Trucking, Inc.	Leo Brown	Minority	\$4,468.75	0.01%	\$4,468.75	0.01%
Scope: Trucking						
Johnson & Johnson Construction	Johnson & Johnson	Minority	\$3,208.75	0.01%	\$3,208.75	0.01%
Scope: Trucking						
T & M Trucking	T & M Trucking	Non-Minority	\$910.00	0.00%	\$910.00	0.00%
Scope: Trucking						
Garcia Brothers Trucking	Garcia Brothers Trucking	Non-Verified Minority	\$783.75	0.00%	\$783.75	0.00%
Scope: Trucking						
CVC Trucking	CVC Trucking	Non-Verified Minority	\$760.00	0.00%	\$760.00	0.00%
Scope: Trucking						
RAW Trucking	Raw Trucking	Minority	\$1,232.50	0.00%	\$1,232.50	0.00%
Scope: Trucking						

Kirby Trucking	Kirby Trucking	Non-Verified Minority	\$1,402.50	0.00%	\$1,402.50	0.00%
Scope: Trucking						
J. Hulick Electric, Inc.	11060-16030	Minority	\$4,066,233.00	8.99%	\$2,200,466.24	4.87%
Scope: Electrical & Fire Alarm						
Tillman Electrical Services	1707	Minority	\$900,000.00	1.99%	\$925,641.33	2.05%
Scope:						
Coreslab Structures	11060-3160-30000	Non-Minority	\$5,846,000.00	12.93%	\$3,693,977.50	8.17%
Scope: Precast Structural Concrete						
Cushing's Commercial Carpet, Inc.	11060-9100	Non-Minority	\$359,500.00	0.80%	\$149,490.00	0.33%
Scope: Flooring						
Houlihan & Associates	11060-9020	Non-Minority	\$1,277,838.00	2.83%	\$0.00	0.00%
Scope:						
Mid- State Terrazzo & Tile	11060-9030	Non-Minority	\$727,500.00	1.61%	\$488,741.95	1.08%
Scope: Tile						
Peoria Roofing & Restoration Co.	11060-7170	Non-Minority	\$295,000.00	0.65%	\$224,465.50	0.50%
Scope: Roofing & Demo						
Lewis Michael Construction Maintenance, Inc.	11060-1390	Minority	\$150,000.00	0.33%	\$81,399.09	0.18%
Scope:						
KONE Inc.	11060-14010	Non-Minority	\$227,000.00	0.50%	\$189,997.20	0.42%
Scope: Elevators						
Montefusco Heating & Sheet Metal Co.	11060-15060	Non-Minority	\$1,227,705.00	2.72%	\$30,482.00	0.07%
Scope: HVAC						
The H3 Group, LLC	11060-5080	Non-Minority	\$442,800.00	0.98%	\$328,872.95	0.73%
Scope: Furnish & Install Steel						
ThyssenKrupp Elevator Corp.	11060-14011	Non-Minority	\$430,025.00	0.95%	\$197,894.25	0.44%
Scope: Elevators						
Dries Brothers Plumbing, Inc.	11060-15030	Non-Minority	\$1,134,820.00	2.51%	\$158,033.50	0.35%
Scope: Plumbing						
Human Capital Development, LLC	2	Minority	\$30,000.00	0.07%	\$15,000.00	0.03%
Scope: ePrism Licensing						
Thompson Brothers, Inc.	11060-8020	Minority	\$1,200,000.00	2.65%	\$563,641.16	1.25%
Scope: Finish Carpentry Install						
Associated Constructors Company, Inc.	11060-9020	Non-Minority	\$3,784,460.00	8.37%	\$1,452,782.90	3.21%
Scope: Framing, Drywall, EIFS, Gypsum Board, Ceilings						
Contech Engineered Solutions LLC	11060-5645	Non-Minority	\$253,116.00	0.56%	\$75,934.80	0.17%

Scope: Pedestrian Walkway (Material Only)						
Commercial Glass Co., Inc.	11060-8090	Non-Minority	\$336,340.00	0.74%	\$265,820.50	0.59%
Scope: Glass & Glazing						
J.J. Braker and Sons, Inc.	11060-4060-30000	Non-Minority	\$228,100.00	0.50%	\$29,735.00	0.07%
Scope: Masonry						
Kreiling Roofing Company	11060-7130-40000	Non-Minority	\$149,774.00	0.33%	\$7,427.10	0.02%
Scope: Roofing						
CONNIES COMMERCIAL CLEANING CO	11060-1410	Minority	\$60,000.00	0.13%	\$55,673.42	0.12%
Scope: Cleaning						
Joseph Construction Co. of Central Illinois	11060-6020	Non-Verified Minority	\$15,000.00	0.03%	\$11,616.00	0.03%
Scope: Finish Carpentry Work						

Payment Recipient Summary

Demographic Information		Gender Information			Certification Information		
Demographic	Population	Male	Female	Unknown	US - MBE	US - DBE	US - WBE
Unspecified	1 \$1,232.50 (0.00%)	1 \$1,232.50 (0.00%)				1 \$1,232.50 (0.00%)	
Black	10 \$2,093,175.73 (4.63%)	8 \$1,463,288.56 (3.24%)	2 \$629,887.17 (1.39%)		10 \$2,093,175.73 (4.63%)		1 \$55,673.42 (0.12%)
Caucasian	1 \$1,274,824.91 (2.82%)		1 \$1,274,824.91 (2.82%)				1 \$1,274,824.91 (2.82%)
Native American	1 \$563,641.16 (1.25%)	1 \$563,641.16 (1.25%)			1 \$563,641.16 (1.25%)		
Asian	0 \$0.00 (0.00%)						
Asian Pacific	0 \$0.00 (0.00%)						
Hispanic	1 \$740,171.70 (1.64%)	1 \$740,171.70 (1.64%)			1 \$740,171.70 (1.64%)		
Latin American	0 \$0.00 (0.00%)						
Subcontinent Asian	0 \$0.00 (0.00%)						
Other	0 \$0.00 (0.00%)						
Non- Minority	25 \$20,990,701.00 (46.43%)			25 \$20,990,701.00 (46.43%)			
TOTALS	39 \$25,663,747.00 (56.76%)	11 \$2,768,333.92 (6.12%)	3 \$1,904,712.08 (4.21%)	25 \$20,990,701.00 (46.43%)	12 \$3,396,988.59 (7.51%)	1 \$1,232.50 (0.00%)	2 \$1,330,498.33 (2.94%)

Employment Breakdown: Unspecified Demographic

Trade	Gender											
	Male			Female			Unspecified			Total		
	Count	Hours		Count	Hours		Count	Hours		Count	Hours	
							2	40	0.02%	2	40	0.02%
TOTALS							2	40	0.02%	2	40	0.02%

Employment Breakdown: Black Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
OPERATOR	3	257	0.13%						3	257	0.13%
CREW CLEANING	2	296	0.15%						2	296	0.15%
SPRINKLERFITTER	4	2281.5	1.12%						4	2281.5	1.12%
GLAZIER	2	168	0.08%						2	168	0.08%
APPRETICE				1	16.5	0.01%			1	16.5	0.01%
OWNER	1	19.75	0.01%						1	19.75	0.01%
	2	73.3	0.04%	2	244	0.12%			4	317.3	0.16%
INSIDE	2	80	0.04%						2	80	0.04%
OPERATINF ENGINEER	1	11.5	0.01%						1	11.5	0.01%
CEMENT MASON	2	16	0.01%						2	16	0.01%
ELECTRICIAN	4	3083	1.51%						4	3083	1.51%
OPERATING ENGINEER	1	3.5	0.00%						1	3.5	0.00%
BRICKLAYER	3	585	0.29%						3	585	0.29%
PAINTER	1	1236	0.61%						1	1236	0.61%
LABORER	21	4302	2.11%	3	1417.5	0.69%			24	5719.5	2.80%
IRON WORKER	3	215	0.11%						3	215	0.11%
OWNER - DESIGN AIR INC	3	59	0.03%						3	59	0.03%
STEAMFITTER	1	1133	0.56%						1	1133	0.56%
CARPENTER	6	2149	1.05%						6	2149	1.05%
WIREMAN	2	319	0.16%						2	319	0.16%
CREW CLANING				1	5.5	0.00%			1	5.5	0.00%
TOTALS	64	16287.55	7.98%	7	1683.5	0.83%			71	17971.05	8.81%

Contract: Pere Marquette - Courtyard

Employment Breakdown: Caucasian Demographic

Trade	Gender											
	Male			Female			Unspecified			Total		
	Count	Hours		Count	Hours		Count	Hours		Count	Hours	
OPERATOR	30	1278.5	0.63%	2	1955.5	0.96%				32	3234	1.59%
POWER EQUIPMENT OPERATOR	1	17	0.01%							1	17	0.01%
PAINTER	33	10955.5	5.37%	4	1424	0.70%				37	12379.5	6.07%
TAPER / PAINTERS	1	38	0.02%							1	38	0.02%
GLAZIER	8	1038	0.51%	1	379.5	0.19%	3	76	0.04%	12	1493.5	0.73%
TAPER	1	40	0.02%							1	40	0.02%
CARPENTER	110	32159.25	15.76%				2	0	0.00%	112	32159.25	15.76%
PAINTER / TAPER	5	1977	0.97%							5	1977	0.97%
	27	2037	1.00%	1	24	0.01%				28	2061	1.01%
SHEET METAL WORKER	51	12580.55	6.17%	1	2	0.00%				52	12582.55	6.17%
CREW CLEANING	2	161	0.08%	1	224	0.11%				3	385	0.19%
PLUMBER	36	17374.5	8.52%	1	514.5	0.25%				37	17889	8.77%
SPRINKLERFITTER	19	2205	1.08%							19	2205	1.08%
FINISHER	3	42	0.02%							3	42	0.02%
CEMENT MASON	25	2189.5	1.07%							25	2189.5	1.07%
BRICKLAYER	71	10447.5	5.12%				1	46	0.02%	72	10493.5	5.14%
PLASTERER	5	92.5	0.05%							5	92.5	0.05%
STEAMFITTER	42	12910	6.33%							42	12910	6.33%
CARPENTER	1	40	0.02%							1	40	0.02%
LABORERS	1	78	0.04%							1	78	0.04%
LABORER	117	21921.5	10.75%	4	1328	0.65%				121	23249.5	11.40%
TAPER	14	2367.5	1.16%							14	2367.5	1.16%
OPERATING ENGINEERS	1	32	0.02%							1	32	0.02%
TILE SETTER	8	1311.5	0.64%							8	1311.5	0.64%
PAINTERS	1	3	0.00%							1	3	0.00%
ELECTRICIAN	57	27893.5	13.67%				2	0	0.00%	59	27893.5	13.67%
APPRENTICE ELECTRICIAN	5	313	0.15%							5	313	0.15%
OPERATING ENGINEER	6	578.5	0.28%	1	72	0.04%				7	650.5	0.32%
TOTALS	681	162081.3	79.45%	16	5923.5	2.90%	8	122	0.06%	705	168126.8	82.41%

Employment Breakdown: Native American Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
OPERATOR	1	8	0.00%						1	8	0.00%
CARPENTER	5	513	0.25%						5	513	0.25%
CARPENTER FOREMAN	1	8	0.00%						1	8	0.00%
MANAGER	1	0	0.00%						1	0	0.00%
TOTALS	8	529	0.26%						8	529	0.26%

Employment Breakdown: Asian Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
SHEET METAL WORKER	1	1224.5	0.60%						1	1224.5	0.60%
PLUMBER	1	312	0.15%						1	312	0.15%
LABORER	3	695	0.34%						3	695	0.34%
TOTALS	5	2231.5	1.09%						5	2231.5	1.09%

Employment Breakdown: Hispanic Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
CREW CLEANING	1	192	0.09%						1	192	0.09%
SPRINKLERFITTER	1	1226	0.60%						1	1226	0.60%
	2	80	0.04%						2	80	0.04%
TILE FINISHER	1	56	0.03%						1	56	0.03%
PAINTER	6	1200	0.59%						6	1200	0.59%
LABORER	33	8934.5	4.38%						33	8934.5	4.38%
IRON WORKER	1	8	0.00%						1	8	0.00%
SHEET METAL WORKER	1	30	0.01%						1	30	0.01%
STEAMFITTER	1	1156.5	0.57%						1	1156.5	0.57%
TILE FITTER	1	332	0.16%						1	332	0.16%
TILE SETTER	4	294	0.14%						4	294	0.14%
CARPENTER	2	1188	0.58%						2	1188	0.58%
PAINTER / TAPER	1	408	0.20%						1	408	0.20%
TOTALS	55	15105	7.40%						55	15105	7.40%

Employment Breakdown: Demographic Summary

Demographic	Gender											
	Male			Female			Unspecified			Total		
	Count	Hours		Count	Hours		Count	Hours		Count	Hours	
Unspecified							2	40	0.02%	2	40	0.02%
Black	56	16287.55	7.98%	6	1683.5	0.83%				62	17971.05	8.81%
Caucasian	638	162081.3	79.45%	14	5923.5	2.90%	8	122	0.06%	660	168126.8	82.41%
Native American	6	529	0.26%							6	529	0.26%
Asian	5	2231.5	1.09%							5	2231.5	1.09%
Asian Pacific												
Hispanic	52	15105	7.40%							52	15105	7.40%
Latin American												
Subcontinent Asian												
Other												
TOTALS	757	196234.35	96.19%	20	7607	3.73%	10	162	0.08%	787	204003.35	100.00%

Employment Breakdown: Apprenticeship Summary

Demographic	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
Unspecified											
Black	9	2145.3	1.05%	3	266	0.13%			12	2411.3	1.18%
Caucasian	85	30217.05	14.81%	1	248	0.12%			86	30465.05	14.93%
Native American	2	161.5	0.08%						2	161.5	0.08%
Asian	1	312	0.15%						1	312	0.15%
Asian Pacific											
Hispanic	6	2133	1.05%						6	2133	1.05%
Latin American											
Subcontinent Asian											
Other											
TOTALS	103	34968.85	17.14%	4	514	0.25%			107	35482.85	17.39%
