

Marriott Hotel Projects

February 2013 Progress Report



Report Dated: March 14, 2013



Marriott Hotel Projects Progress Report

This is the monthly report prepared by Dewberry Architects Inc. for the month of February 2013. It covers construction activities for the four components of the project; parking deck, pedestrian bridge, Pere Marquette Hotel, and the Marriott Courtyard Hotel. The ePrismSoft Compliance System Executive Summary Report, dated March 13, 2013, for EEO monitoring is attached.

Parking Deck

Progress Summary:

The parking deck is substantially complete. Directional signage has been installed. The generator has been set. Phone lines have been installed for the elevator and fire alarm system. Fire alarm and sprinkler systems have been certified. The final elevator and City of Peoria inspections were scheduled for the first week of March. The concrete in the alley has been poured up to the Marriott Courtyard site. As of the writing of this report, the elevator and parking deck has passed the inspections and the parking deck has been turned over to the Developer. The parking deck is currently open and operating.

Forthcoming Items:

Final exterior painting and EFIS installation will be completed when the weather permits.

Photos:



Concrete paving in alley

Pedestrian Bridge

Progress Summary:

The Comcast lines have been relocated. The concrete foundations have been poured. Existing sewer lines found during the excavation for the foundation have also been relocated. A temporary walkway has been provided along Fulton Street for pedestrian access around this portion of the work.

Forthcoming Items:

The foundation wall will be formed and poured. When the walls are built, field measurements will be taken for the bridge trusses.

Photos:



Foundation work



Footing work

Pere Marquette Hotel

Progress Summary:

The corridor carpet and FFE have been installed on the 10th floor. Final touch ups and life safety device installation is underway on the 10th floor. The 9th floor is nearing completion with activities including corridor carpet installation, FFE installation, and life safety device installation.

The FFE installation is in process on floors 4 through 9. MEP is trimming their devices on floors 3 through 8. Glass shower doors are being installed on the 3rd and 4th floors. Room carpet is being installed on the 2nd and 3rd floors. Doors and valances are being installed on the 2nd, 3rd, and 11th floors. Painting and wall covering installation is ongoing on the 11th floor. MEP rough-in is complete on the 12th floor with wall patching continuing.

Work in the basement, 1st floor, ballrooms, mezzanine, and 2nd floor is progressing with multiple concurrent activities. MEP rough-ins are being finalized. Equipment is being connected. Framing is nearing completion. Drywall is being installed, taped and sanded. Floor tile, ceiling grid, paint, and wall covering are being installed. Doors and hardware are being installed. Work on the grand staircase is underway.

The heat pump system is fully pressurized and in the process of being commissioned. Boilers on the 13th floor have been commissioned. The fire alarm system is being tested. The passenger elevators are being refurbished. The freight elevator door has been replaced and the elevator is back in operation.

Roofing work on the low roof has been dependant on weather conditions. The roofing membrane is anticipated to be installed as soon as weather conditions allow. HVAC equipment has been set on the lower roof and connections are being made.

Forthcoming Items:

FF&E items will continue to be shipped including some of the specialty vanities, carpet for the ballrooms, and light fixtures.

Photos:



FFE installation on the 10th floor



FFE installation on the 10th floor



Guestroom bathroom with FFE on 10th floor



Guestroom bathroom with shower door



Corridor carpet on 10th floor



Carpet pad in guest room on 2nd floor



Tile in vending room



Ceiling grid installation in exercise room




Radiant heat covers on Ballroom level



Painting on Ballroom level



Ceiling patching on Ballroom level

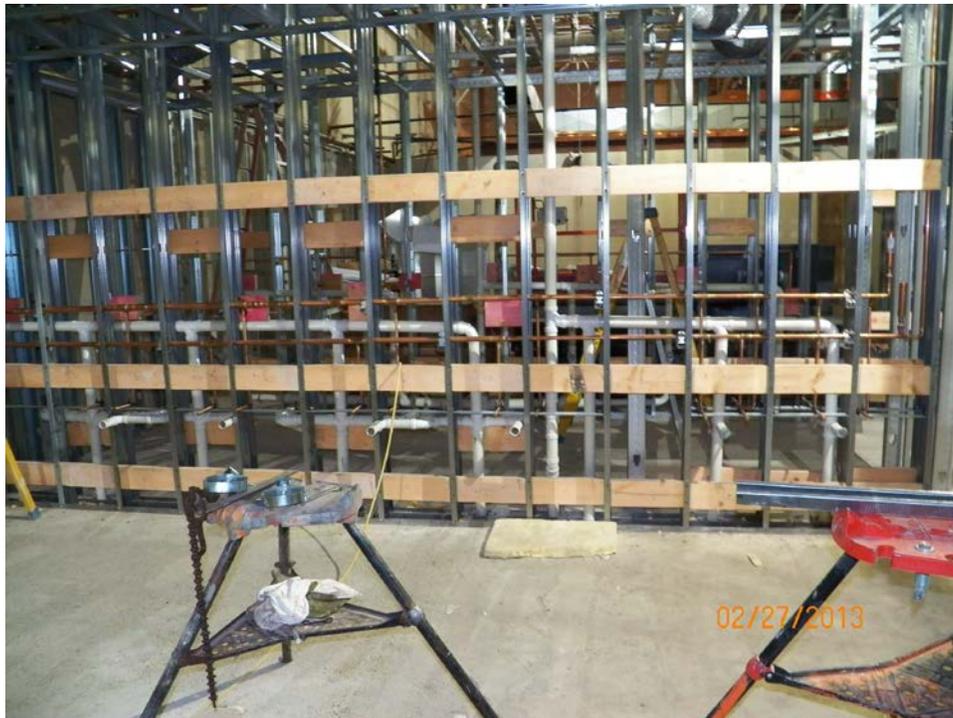

Ballroom level restroom rough-ins



Taping drywall on 1st floor



Floor tile installation on 1st floor



Grand stair from 1st floor



New finishes in passenger elevator cab



Pressurized heat pump system



HVAC equipment on lower roof

Courtyard

Progress Summary:

Demolition of the buildings is underway. Precast panels are in production and approximately 65% are made and ready for shipment.

Forthcoming Items:

Foundation work for the basement is anticipated to start in March while the demolition work is being completed.

Photos:



Building demolition underway



Building demolition progress



Building demolition progress



Building demolition progress

Schedule

The construction schedule for the Pere Marquette was adjusted to June 2013. Current targeted milestones are listed below.

Milestones:

Parking Deck	Open
Pere Marquette Substantial Completion	June 2013
Pere Marquette Opening	End of June 2013 (Contingent on Marriott)

Financial

The project construction costs remain within budget. There were no new change orders this month. The construction contract with Core Construction Services, Inc. covers the construction of the parking deck, pedestrian bridge, the Pere Marquette, and the Courtyard by Marriott.

Construction Cost Status

(Includes pay application No. 12 for the month of February 2013)

Original Contract Sum	\$44,000,000.00
Net Change Orders	\$1,214,148.00
Contract Sum to Date	\$45,214,148.00
Total Complete to Date	\$27,516,093.92
Percent Complete	61%
Retainage	\$2,509,300.97
Total Paid to Date	\$25,006,792.95
Balance to Finish	\$20,207,355.05

EEO

Project Goals:

Enterprise Level: 10% MBE and 5% WBE
 Labor Utilization: 18% Minority and 3% Female

Progress Summary:

Verified MBE firms under contract have increased slightly to 9.81% of the total construction cost. Due to the multiple phase nature of the project, only approximately \$38 million of the \$45 million value has been committed (contracted). Comparing the current MBE contracts to the total committed, the MBE portion still represents 11.51%. In addition there are currently 4 non-verified MBE firms. These are firms that are under contract and are having their status confirmed. Efforts are continuing to contract additional MBE firms for portions of the uncommitted (non-contracted) work.

For the WBE portion; J. Hulick Electric, Inc. and Connies Commercial Cleaning are identified. The WBE contracted value is at 7.11%. Connie's Commercial Cleaning is both a MBE and WBE and is reflected in both Contracted Values. Since the value cannot be counted twice in the subtotal, \$50,000 has been subtracted to arrive at the \$38,527,554.80 subtotal.

The Human Capital Development report now also includes confirmed payments to MBE and WBE firms, as well as, a breakdown of payments by demographic group. For the MBE and WBE firms, this is indicated as the "Actual Value" and is reflected in the chart below. As anticipated, these figures continue to increase as contractors are paid.

Enterprise Level Summary (Project Goals: 10% MBE and 5% WBE)

Current results based on Human Capital Development, LLC Executive Contract Summary Report dated 3/13/2013.

	Contracted Values	Percentage of Total Contract	Percentage of Committed Work	Actual Value (Confirmed Payments)
MBE	\$4,436,398.00	9.81%	11.51%	\$2,592,592.29
WBE*	\$3,216,233.00	7.11%	8.35%	\$1,257,404.41
NON-VERIFIED Minority	\$7,946.25	0.02%	0.02%	\$2,946.25
NON-MINORITY	\$30,916,977.55	68.38%	80.25%	\$18,756,873.23
COMMITTED WORK (Subtotal)	\$38,527,554.80	85.21%	100.13%	\$22,609,816.18
UNCOMMITTED WORK**	\$6,686,593.20	14.79%		
TOTALS	\$45,214,148.00	100.00%		

* See discussion above concerning WBE.

**The Uncommitted Work is work for which there are no contracts yet.

Minority labor utilization is near goal at 17.54% and the Female utilization is at 3.79%. The minority labor utilization has been falling slightly for several months. The contractor is aware of this trend and is making efforts to increase the utilization.

Labor Utilization Summary (Project Goals: 18% Minority and 3% Female)

Current results based on Human Capital Development, LLC Executive Contract Summary Report dated 3/13/2013.

	Current Labor Hours	Percentage of Total
Minority	31,367.75	17.54%
Female	6,778.50	3.79%
Non-Minority/Female	142,195.30	79.53%
Total	178,794.05	

Please note when reviewing the Human Capital Development report in the Labor Utilization chart that the total for line items Minority, Female, and Non-Minority/Female shows as 178,794.05 hours, however, the hours listed for these lines adds up to 180,341.55 hours. There are 1,547.5 female minority hours that are reported under both the Female and Minority items. Since these hours cannot be counted twice for the total, 1,547.5 hours has been subtracted out to arrive at the 178,794.05 hour total. Adding the 1,377.5 hours to the 178,794.05 equals 180,341.55 hours which is the same total arrived at by adding the hours reported for each line item.

Also, when reviewing the Human Capital Development report you will note a difference between the total number of employees of each Demographic Employment Breakdown and the employee count shown in the Demographic Summary Chart. This difference is due the fact that some employees perform more than one trade tasks listed in the Demographic Employment Breakdown. As an example, the Black Demographic Employment Breakdown shows 55 males for a total of 13,807.75 hours. When you look at the Demographic Summary chart under Black Male, you see a count of 49 for 13,807.75 hours. Each Demographic Employment Breakdown Chart shows how many employees perform which tasks while the Demographic Summary chart shows the total number of employees within a specific demographic.

In the Human Capital Development report you will find the current List of Subcontractors that list all those subcontractors under contract. Please note that this list indicates each contractor’s gross contract amount. Some of the contractors are subcontractors to other contractors on this list. The reporting software nets these values when reporting them in the Enterprise Level Summary chart.

The Human Capital Development report also includes an “Employment Breakdown: Apprenticeship Summary” chart. This chart was added in support of Illinois Project Labor Agreements Act HB 2987.

During Dewberry’s periodic site visits, we have casually observed EEO participation and have found them to be consistent with the figures presented.

ePrismSoft Compliance System



Executive Contract Summary

Contract Name: Pere Marquette - Courtyard
Report Period: April 2012 to February 2013
Contractor: CORE Construction

Contract: Pere Marquette - Courtyard

Enterprise Level

Goal	Contract Planned Value	Actual Value	% of Plan	% of Actual
5.00% US - WBE or US - FBE	\$3,216,233.00	\$1,143,162.01	7.11%	2.53%
10.00% US - MBE or US - DBE	\$4,436,398.00	\$3,080,249.91	9.81%	6.81%
Total Minority Subs	\$7,602,631.00	\$4,208,109.92	16.81%	9.31%
Non- Verified Minority Subs	\$7,946.25	\$2,946.25	0.02%	0.01%
Total Non- Minority Subs	\$30,916,977.55	\$18,460,185.23	68.38%	40.83%
Amount Not Yet Allocated	\$6,686,593.20	\$0.00	14.79%	0.00%
Contract Totals	\$45,214,148.00	\$22,671,241.40	100.00%	50.14%

Non- Verified Minority Subcontractors

Contractor Name	Contract Name	Contract Amount	Contract Payments
Garcia Brothers Trucking	Garcia Brothers Trucking	\$783.75	\$783.75
CVC Trucking	CVC Trucking	\$760.00	\$760.00
Kirby Trucking	Kirby Trucking	\$1,402.50	\$1,402.50
Joseph Construction Co. of Central Illinois	Joseph Construction Co. of Central Illinois	\$5,000.00	\$0.00

Main Contract Change Orders

Change ID	Date	Previous Amount	Change Amount	New Amount
CO #4	12/04/2012	\$44,000,000.00	\$432,148.00	\$44,432,148.00
	01/31/2013	\$44,432,148.00	\$782,000.00	\$45,214,148.00
Total Change			\$1,214,148.00	

Labor Utilization

Goal	Labor Hours	Percent of Total
90.00% Resident Workforce in IL state	176,347.55	97.57%
18.00% Minority Workforce	31,630.75	17.50%
3.00% Female Workforce	6,778.50	3.75%
Non Minority/ Female	143,870.80	79.60%
Total Contract Hours	180,732.55	100%

List of Subcontractors

Contractor Name	Contract Number	Contractor Status	Contract Amount		Contract Payments	
Human Capital Development, LLC	2012	Minority	\$40,000.00	0.09%	\$15,000.00	0.03%
Scope: Consulting						
Core Construction Services of Illinois Inc.	Internal Work Order	Non-Minority	\$4,343,191.80	9.61%	\$5,129,497.23	11.34%
Scope:						
Valor Technologies, Inc.	11060-2052	Minority	\$980,000.00	2.17%	\$735,406.20	1.63%
Scope: Abatement						
Otto Baum Company, Inc.	11060-4060	Non-Minority	\$1,802,237.00	3.99%	\$1,578,438.90	3.49%
Scope: Masonry Restoration; Cast- in- Place Concrete; Paving; Excavation; Storm Sewer; Masonry						
Central Illinois Rebar Installers, Inc.	12-306-1	Minority	\$75,280.00	0.17%	\$61,502.30	0.14%
Scope:						
The PIPCO Companies, LTD.	11060-15030	Non-Minority	\$7,302,410.00	16.15%	\$5,510,323.42	12.19%
Scope: Plumbing; Fire Protection; HVAC						
Design Air Inc.	002	Minority	\$502,208.00	1.11%	\$357,068.34	0.79%
Scope: Plumbing						
VOGUE PAINTING & DECORATING	11060-9110	Non-Minority	\$1,463,105.00	3.24%	\$663,131.91	1.47%
Scope: Painting & Ceiling Patching						
Ridge Painting	13	Minority	\$500,000.00	1.11%	\$401,886.46	0.89%
Scope:						
River City Demolition	11060-2050	Non-Minority	\$358,400.00	0.79%	\$348,101.32	0.77%
Scope: Demolition						
KENNEL Trucking	KENNEL Trucking	Non-Minority	\$5,567.50	0.01%	\$5,567.50	0.01%
Scope: Trucking						
Leo Brown Trucking, Inc.	Leo Brown	Minority	\$4,468.75	0.01%	\$4,468.75	0.01%
Scope: Trucking						
Johnson & Johnson Construction	Johnson & Johnson	Minority	\$3,208.75	0.01%	\$3,208.75	0.01%
Scope: Trucking						
T & M Trucking	T & M Trucking	Non-Minority	\$910.00	0.00%	\$910.00	0.00%
Scope: Trucking						
Garcia Brothers Trucking	Garcia Brothers Trucking	Non-Verified Minority	\$783.75	0.00%	\$783.75	0.00%
Scope: Trucking						
CVC Trucking	CVC Trucking	Non-Verified Minority	\$760.00	0.00%	\$760.00	0.00%
Scope: Trucking						
RAW Trucking	Raw Trucking	Minority	\$1,232.50	0.00%	\$1,232.50	0.00%
Scope: Trucking						

Kirby Trucking	Kirby Trucking	Non-Verified Minority	\$1,402.50	0.00%	\$1,402.50	0.00%
Scope: Trucking						
J. Hulick Electric, Inc.	11060-16030	Minority	\$4,066,233.00	8.99%	\$1,959,166.24	4.33%
Scope: Electrical & Fire Alarm						
Tillman Electrical Services	1707	Minority	\$900,000.00	1.99%	\$831,306.23	1.84%
Scope:						
Coreslab Structures	11060-3160-30000	Non-Minority	\$5,846,000.00	12.93%	\$3,088,849.50	6.83%
Scope: Precast Structural Concrete						
Cushing's Commercial Carpet, Inc.	11060-9100	Non-Minority	\$359,500.00	0.80%	\$52,920.00	0.12%
Scope: Flooring						
Houlihan & Associates	11060-9020	Non-Minority	\$1,277,838.00	2.83%	\$0.00	0.00%
Scope:						
Mid- State Terrazzo & Tile	11060-9030	Non-Minority	\$727,500.00	1.61%	\$284,265.00	0.63%
Scope: Tile						
Peoria Roofing & Restoration Co.	11060-7170	Non-Minority	\$295,000.00	0.65%	\$224,465.50	0.50%
Scope: Roofing & Demo						
Lewis Michael Construction Maintenance, Inc.	11060-1390	Minority	\$150,000.00	0.33%	\$75,227.22	0.17%
Scope:						
KONE Inc.	11060-14010	Non-Minority	\$227,000.00	0.50%	\$89,440.20	0.20%
Scope: Elevators						
Montefusco Heating & Sheet Metal Co.	11060-15060	Non-Minority	\$1,227,705.00	2.72%	\$22,914.00	0.05%
Scope: HVAC						
The H3 Group, LLC	11060-5080	Non-Minority	\$442,800.00	0.98%	\$318,805.20	0.71%
Scope: Furnish & Install Steel						
ThyssenKrupp Elevator Corp.	11060-14011	Non-Minority	\$430,025.00	0.95%	\$192,978.00	0.43%
Scope: Elevators						
Dries Brothers Plumbing, Inc.	11060-15030	Non-Minority	\$1,151,820.00	2.55%	\$146,502.00	0.32%
Scope: Plumbing						
Human Capital Development, LLC	2	Minority	\$30,000.00	0.07%	\$15,000.00	0.03%
Scope: ePrism Licensing						
Thompson Brothers, Inc.	11060-8020	Minority	\$1,200,000.00	2.65%	\$563,641.16	1.25%
Scope: Finish Carpentry Install						
Associated Constructors Company, Inc.	11060-9020	Non-Minority	\$3,784,460.00	8.37%	\$1,325,457.90	2.93%
Scope: Framing, Drywall, EIFS, Gypsum Board, Ceilings						
Contech Engineered Solutions LLC	11060-5645	Non-Minority	\$253,116.00	0.56%	\$75,934.80	0.17%

Scope: Pedestrian Walkway (Material Only)						
Commercial Glass Co., Inc.	11060-8090	Non-Minority	\$336,340.00	0.74%	\$205,267.50	0.45%
Scope: Glass & Glazing						
J.J. Braker and Sons, Inc.	11060-4060-30000	Non-Minority	\$228,100.00	0.50%	\$28,170.00	0.06%
Scope: Masonry						
Kreiling Roofing Company	11060-7130-40000	Non-Minority	\$149,774.00	0.33%	\$7,036.20	0.02%
Scope: Roofing						
CONNIES COMMERCIAL CLEANING CO	11060-1410	Minority	\$50,000.00	0.11%	\$15,302.00	0.03%
Scope: Cleaning						
Joseph Construction Co. of Central Illinois	11060-6020	Non-Verified Minority	\$5,000.00	0.01%	\$0.00	0.00%
Scope: Finish Carpentry Work						

Payment Recipient Summary

Demographic Information		Gender Information			Certification Information		
Demographic	Population	Male	Female	Unknown	US - MBE	US - DBE	US - WBE
Unspecified	1 \$1,232.50 (0.00%)	1 \$1,232.50 (0.00%)				1 \$1,232.50 (0.00%)	
Black	10 \$1,779,970.05 (3.94%)	8 \$1,362,781.59 (3.01%)	2 \$417,188.46 (0.92%)		10 \$1,779,970.05 (3.94%)		1 \$15,302.00 (0.03%)
Caucasian	1 \$1,127,860.01 (2.49%)		1 \$1,127,860.01 (2.49%)				1 \$1,127,860.01 (2.49%)
Native American	1 \$563,641.16 (1.25%)	1 \$563,641.16 (1.25%)			1 \$563,641.16 (1.25%)		
Asian	0 \$0.00 (0.00%)						
Asian Pacific	0 \$0.00 (0.00%)						
Hispanic	1 \$735,406.20 (1.63%)	1 \$735,406.20 (1.63%)			1 \$735,406.20 (1.63%)		
Latin American	0 \$0.00 (0.00%)						
Subcontinent Asian	0 \$0.00 (0.00%)						
Other	0 \$0.00 (0.00%)						
Non- Minority	24 \$18,463,131.48 (40.83%)			24 \$18,463,131.48 (40.83%)			
TOTALS	38 \$22,671,241.40 (50.14%)	11 \$2,663,061.45 (5.89%)	3 \$1,545,048.47 (3.42%)	24 \$18,463,131.48 (40.83%)	12 \$3,079,017.41 (6.81%)	1 \$1,232.50 (0.00%)	2 \$1,143,162.01 (2.53%)

Employment Breakdown: Unspecified Demographic

Trade	Gender										
	Male		Female			Unspecified			Total		
	Count	Hours	Count	Hours	Count	Hours	Count	Hours			
CREW CLEANING			1	32	0.02%	1	24	0.01%	2	56	0.03%
						2	40	0.02%	2	40	0.02%
TOTALS			1	32	0.02%	3	64	0.04%	4	96	0.05%

Employment Breakdown: Black Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
OPERATOR	3	224.5	0.12%						3	224.5	0.12%
SPRINKLERFITTER	4	1618	0.90%						4	1618	0.90%
GLAZIER	1	112	0.06%						1	112	0.06%
APPRETICE				1	130	0.07%			1	130	0.07%
OWNER	1	19.75	0.01%						1	19.75	0.01%
INSIDE	2	80	0.04%						2	80	0.04%
OPERATINF ENGINEER	1	11.5	0.01%						1	11.5	0.01%
CEMENT MASON	2	16	0.01%						2	16	0.01%
ELECTRICIAN	3	2509	1.39%						3	2509	1.39%
OPERATING ENGINEER	1	3.5	0.00%						1	3.5	0.00%
BRICKLAYER	3	585	0.32%						3	585	0.32%
PAINTER	1	1135	0.63%						1	1135	0.63%
LABORER	20	4070.5	2.25%	3	1417.5	0.78%			23	5488	3.04%
IRON WORKER	3	215	0.12%						3	215	0.12%
OWNER - DESIGN AIR INC	3	59	0.03%						3	59	0.03%
STEAMFITTER	1	1054	0.58%						1	1054	0.58%
CARPENTER	4	1839	1.02%						4	1839	1.02%
WIREMAN	2	319	0.18%						2	319	0.18%
TOTALS	55	13870.75	7.67%	4	1547.5	0.86%			59	15418.25	8.53%

Employment Breakdown: Caucasian Demographic

Trade	Gender											
	Male			Female			Unspecified			Total		
	Count	Hours		Count	Hours		Count	Hours		Count	Hours	
OPERATOR	27	1226.5	0.68%	1	1673	0.93%				28	2899.5	1.60%
POWER EQUIPMENT OPERATOR	1	17	0.01%							1	17	0.01%
PAINTER	26	8944.5	4.95%	4	1275	0.71%				30	10219.5	5.65%
TAPER / PAINTERS	1	38	0.02%							1	38	0.02%
GLAZIER	8	892	0.49%	1	334.5	0.19%	3	76	0.04%	12	1302.5	0.72%
TAPER	1	40	0.02%							1	40	0.02%
CARPENTER	89	28222.25	15.62%				2	0	0.00%	91	28222.25	15.62%
PAINTER / TAPER	5	1722	0.95%							5	1722	0.95%
	20	1274.5	0.71%							20	1274.5	0.71%
SHEET METAL WORKER	50	11233.55	6.22%	1	2	0.00%				51	11235.55	6.22%
PLUMBER	36	15631.5	8.65%	1	514.5	0.28%				37	16146	8.93%
SPRINKLERFITTER	19	1974	1.09%							19	1974	1.09%
FINISHER	3	42	0.02%							3	42	0.02%
CEMENT MASON	22	1811.5	1.00%							22	1811.5	1.00%
BRICKLAYER	69	10387.5	5.75%				1	46	0.03%	70	10433.5	5.77%
PLASTERER	5	92.5	0.05%							5	92.5	0.05%
STEAMFITTER	39	10958.5	6.06%							39	10958.5	6.06%
CARPENTER	1	40	0.02%							1	40	0.02%
LABORERS	1	78	0.04%							1	78	0.04%
LABORER	110	20945.5	11.59%	4	1328	0.73%				114	22273.5	12.32%
TAPER	14	2218.5	1.23%							14	2218.5	1.23%
OPERATING ENGINEERS	1	32	0.02%							1	32	0.02%
TILE SETTER	8	1311.5	0.73%							8	1311.5	0.73%
PAINTERS	1	3	0.00%							1	3	0.00%
ELECTRICIAN	54	23657	13.09%				2	0	0.00%	56	23657	13.09%
APPRENTICE ELECTRICIAN	5	313	0.17%							5	313	0.17%
OPERATING ENGINEER	6	578.5	0.32%	1	72	0.04%				7	650.5	0.36%
TOTALS	622	143684.8	79.50%	13	5199	2.88%	8	122	0.07%	643	149005.8	82.45%

Employment Breakdown: Native American Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
OPERATOR	1	8	0.00%						1	8	0.00%
CARPENTER	4	305	0.17%						4	305	0.17%
CARPENTER FOREMAN	1	8	0.00%						1	8	0.00%
MANAGER	1	0	0.00%						1	0	0.00%
TOTALS	7	321	0.18%						7	321	0.18%

Employment Breakdown: Asian Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
SHEET METAL WORKER	1	1061.5	0.59%						1	1061.5	0.59%
PLUMBER	1	312	0.17%						1	312	0.17%
LABORER	3	695	0.38%						3	695	0.38%
TOTALS	5	2068.5	1.14%						5	2068.5	1.14%

Employment Breakdown: Hispanic Demographic

Trade	Gender										
	Male			Female			Unspecified		Total		
	Count	Hours		Count	Hours		Count	Hours	Count	Hours	
CREW CLEANING	3	72	0.04%						3	72	0.04%
SPRINKLERFITTER	1	1016	0.56%						1	1016	0.56%
	1	24	0.01%						1	24	0.01%
TILE FINISHER	1	56	0.03%						1	56	0.03%
PAINTER	5	966	0.53%						5	966	0.53%
LABORER	33	8507.5	4.71%						33	8507.5	4.71%
IRON WORKER	1	8	0.00%						1	8	0.00%
SHEET METAL WORKER	1	30	0.02%						1	30	0.02%
STEAMFITTER	1	1073.5	0.59%						1	1073.5	0.59%
TILE FITTER	1	332	0.18%						1	332	0.18%
TILE SETTER	4	294	0.16%						4	294	0.16%
CARPENTER	2	1036	0.57%						2	1036	0.57%
PAINTER / TAPER	1	408	0.23%						1	408	0.23%
TOTALS	55	13823	7.65%						55	13823	7.65%

Employment Breakdown: Demographic Summary

Demographic	Gender											
	Male			Female			Unspecified			Total		
	Count	Hours		Count	Hours		Count	Hours		Count	Hours	
Unspecified				1	32	0.02%	3	64	0.04%	4	96	0.05%
Black	49	13870.75	7.67%	4	1547.5	0.86%				53	15418.25	8.53%
Caucasian	585	143684.8	79.50%	12	5199	2.88%	8	122	0.07%	605	149005.8	82.45%
Native American	5	321	0.18%							5	321	0.18%
Asian	5	2068.5	1.14%							5	2068.5	1.14%
Asian Pacific												
Hispanic	53	13823	7.65%							53	13823	7.65%
Latin American												
Subcontinent Asian												
Other												
TOTALS	697	173768.05	96.15%	17	6778.5	3.75%	11	186	0.10%	725	180732.55	100.00%

Employment Breakdown: Apprenticeship Summary

Demographic	Gender											
	Male			Female			Unspecified			Total		
	Count	Hours		Count	Hours		Count	Hours		Count	Hours	
Unspecified				1	32	0.02%	1	24	0.01%	2	56	0.03%
Black	6	1449.5	0.80%	1	130	0.07%				7	1579.5	0.87%
Caucasian	79	26662.05	14.75%							79	26662.05	14.75%
Native American	1	105.5	0.06%							1	105.5	0.06%
Asian	1	312	0.17%							1	312	0.17%
Asian Pacific												
Hispanic	8	1747	0.97%							8	1747	0.97%
Latin American												
Subcontinent Asian												
Other												
TOTALS	95	30276.05	16.75%	2	162	0.09%	1	24	0.01%	98	30462.05	16.85%
